


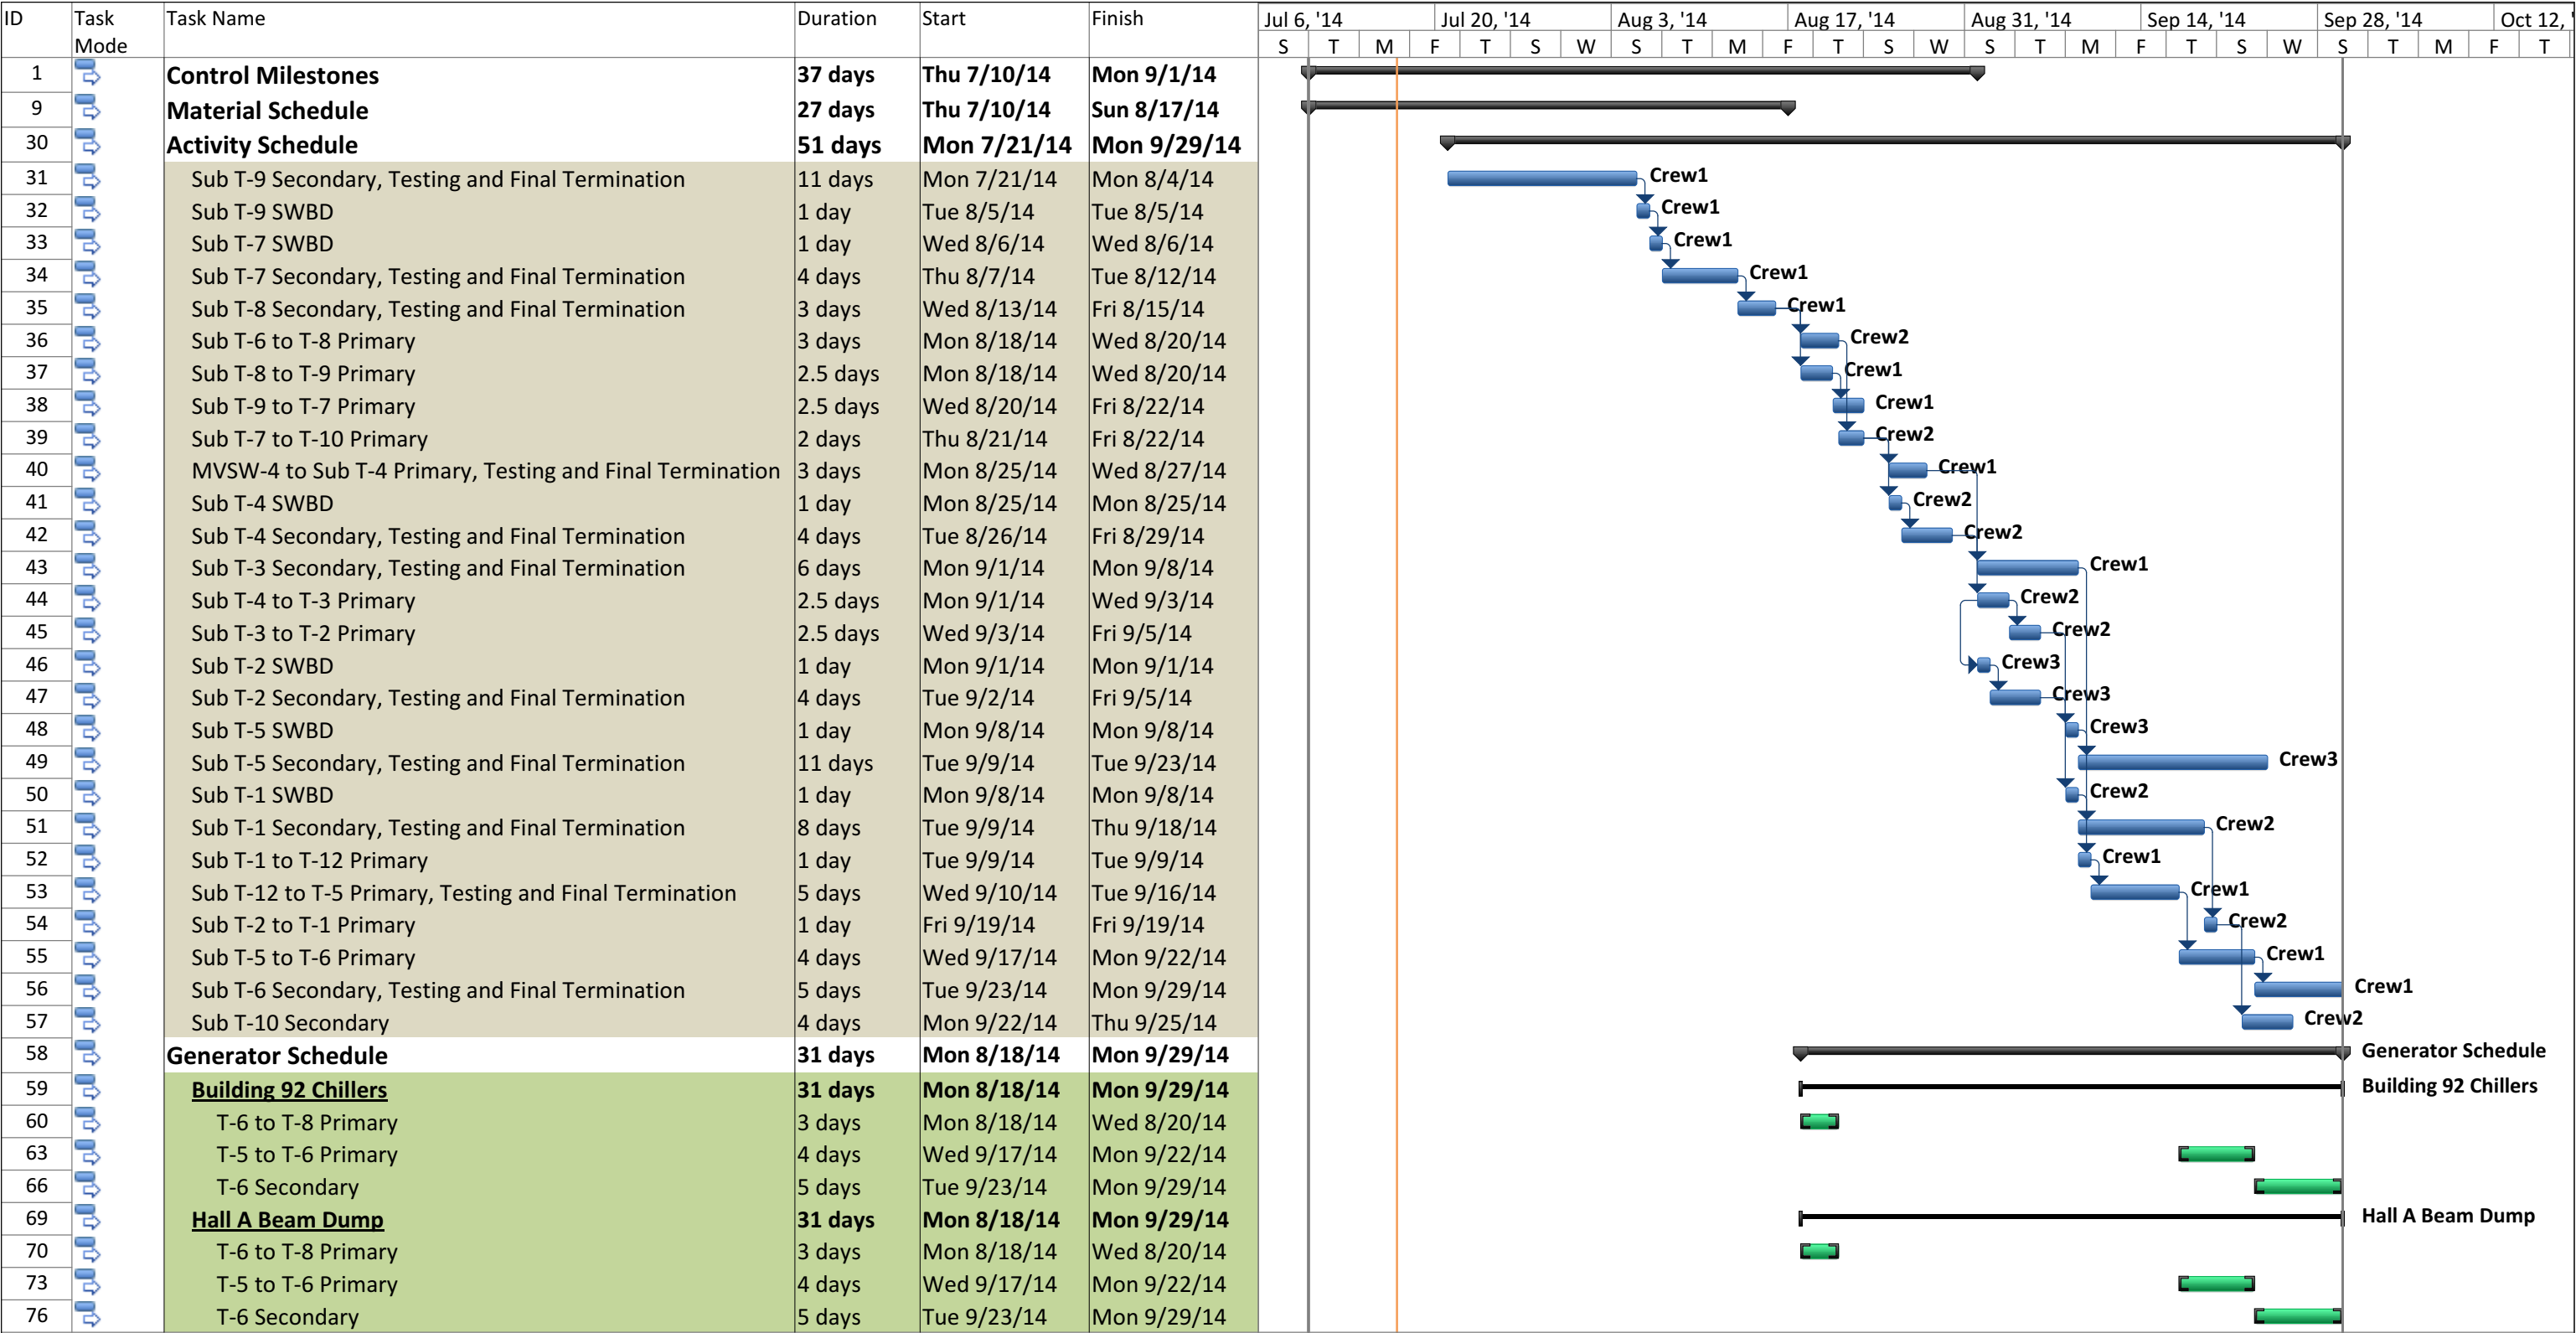

Project: ESRAdvance
Date: Thu 7/17/14

Facility Outage

Region Outage

Outage

Generator Use

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Progress

ID	Task Mode	Task Name	Duration	Start	Finish	Jul 6, '14			Jul 20, '14				Aug 3, '14			Aug 17, '14				Aug 31, '14				Sep 14, '14				Sep 28, '14				Oct 12, '14		
						S	T	M	F	T	S	W	S	T	M	F	T	S	W	S	T	M	F	T	S	W	S	T	M	F	T			
79		Hall C Beam Dump	15 days	Mon 9/1/14	Fri 9/19/14																													
80		T-3 to T-2 Primary	2.5 days	Wed 9/3/14	Fri 9/5/14																													
83		T-2 Switchboard	1 day	Mon 9/1/14	Mon 9/1/14																													
86		T-2 Secondary	4 days	Tue 9/2/14	Fri 9/5/14																													
89		T-2 to T-1 Primary	1 day	Fri 9/19/14	Fri 9/19/14																													
92		Building 98	26 days	Thu 8/21/14	Thu 9/25/14																													
93		T-7 to T-10 Primary	2 days	Thu 8/21/14	Fri 8/22/14																													
96		T-10 Secondary	4 days	Mon 9/22/14	Thu 9/25/14																													
99		Impact Schedule	51 days	Mon 7/21/14	Mon 9/29/14																													
100		End Station Refrigeration	16 days	Wed 8/6/14	Wed 8/27/14																													
101		Offline (T-7 Switchboard)	1 day	Wed 8/6/14	Wed 8/6/14																													
104		Offline (T-7 Secondary)	4 days	Thu 8/7/14	Tue 8/12/14																													
107		Offline (T-8 Secondary)	3 days	Wed 8/13/14	Fri 8/15/14																													
110		Offline (T-6 to T-8 Primary)	3 days	Mon 8/18/14	Wed 8/20/14																													
113		Offline (T-8 to T-9 Primary)	2.5 days	Mon 8/18/14	Wed 8/20/14																													
116		Offline (T-9 to T-7 Primary)	2.5 days	Wed 8/20/14	Fri 8/22/14																													
119		Offline (T-7 to T-10 Primary)	2 days	Thu 8/21/14	Fri 8/22/14																													
122		Offline (MVSW-4 to T-4 Primary)	3 days	Mon 8/25/14	Wed 8/27/14																													
125		LCW Systems	9 days	Wed 9/17/14	Mon 9/29/14																													
126		Offline (T-5 to T-6 Primary)	4 days	Wed 9/17/14	Mon 9/22/14																													
129		Offline (T-6 Secondary)	5 days	Tue 9/23/14	Mon 9/29/14																													
132		Physics Chalet	26 days	Thu 8/21/14	Thu 9/25/14																													
133		Offline (T-7 to T-10 Primary)	2 days	Thu 8/21/14	Fri 8/22/14																													
136		Offline (T-10 Secondary)	4 days	Mon 9/22/14	Thu 9/25/14																													
139		Counting House	20 days	Mon 8/25/14	Fri 9/19/14																													
140		Utility Power	7.5 days	Mon 8/25/14	Wed 9/3/14																													
141		Offline (MVSW-4 to T-4 Primary)	3 days	Mon 8/25/14	Wed 8/27/14																													
144		Offline (T-4 Switchboard)	1 day	Mon 8/25/14	Mon 8/25/14																													
147		Offline (T-4 Secondary)	4 days	Tue 8/26/14	Fri 8/29/14																													
150		Offline (T-4 to T-3 Primary)	2.5 days	Mon 9/1/14	Wed 9/3/14																													
153		Computing Power	6 days	Mon 9/1/14	Mon 9/8/14																													
154		Offline (T-4 to T-3 Primary)	2.5 days	Mon 9/1/14	Wed 9/3/14																													
157		Offline (T-3 to T-2 Primary)	2.5 days	Wed 9/3/14	Fri 9/5/14																													
160		Offline (T-3 Secondary)	6 days	Mon 9/1/14	Mon 9/8/14																													
163		Clean Power	15 days	Mon 9/1/14	Fri 9/19/14																													
164		Offline (T-3 to T-2 Primary)	2.5 days	Wed 9/3/14	Fri 9/5/14																													
167		Offline (T-2 Switchboard)	1 day	Mon 9/1/14	Mon 9/1/14																													
170		Offline (T-2 Secondary)	4 days	Tue 9/2/14	Fri 9/5/14																													
173		Offline (T-2 to T-1 Primary)	1 day	Fri 9/19/14	Fri 9/19/14																													

Project: ESRAdvance
Date: Thu 7/17/14

Facility Outage

Region Outage

Outage

Generator Use

Task

Split

 Milestone

 Summary External Milestone Duration-only Deadline

ID	Task Mode	Task Name	Duration	Start	Finish	Jul 6, '14			Jul 20, '14				Aug 3, '14			Aug 17, '14				Aug 31, '14				Sep 14, '14				Sep 28, '14				Oct 12, '14			
						S	T	M	F	T	S	W	S	T	M	F	T	S	W	S	T	M	F	T	S	W	S	T	M	F	T				
176		Hall A	51 days	Mon 7/21/14	Mon 9/29/14																					Hall A									
177		Utility Power	6 days	Wed 8/13/14	Wed 8/20/14																					Utility Power									
178		Offline (T-8 Secondary)	3 days	Wed 8/13/14	Fri 8/15/14																														
181		Offline (T-8 to T-9 Primary)	3 days	Mon 8/18/14	Wed 8/20/14																														
184		Offline (T-6 to T-8 Primary)	2.5 days	Mon 8/18/14	Wed 8/20/14																														
187		System Power	25 days	Mon 7/21/14	Fri 8/22/14																					System Power									
188		Offline (T-9 Secondary)	11 days	Mon 7/21/14	Mon 8/4/14																														
191		Offline (T-9 Switchboard)	1 day	Tue 8/5/14	Tue 8/5/14																														
194		Offline (T-8 to T-9 Primary)	2.5 days	Mon 8/18/14	Wed 8/20/14																														
197		Offline (T-9 to T-7 Primary)	2.5 days	Wed 8/20/14	Fri 8/22/14																														
200		Clean Power	15 days	Mon 9/1/14	Fri 9/19/14																					Clean Power									
201		Offline (T-2 Switchboard)	1 day	Mon 9/1/14	Mon 9/1/14																														
204		Offline (T-2 Secondary)	4 days	Tue 9/2/14	Fri 9/5/14																														
207		Offline (T-3 to T-2 Primary)	2.5 days	Wed 9/3/14	Fri 9/5/14																														
210		Offline (T-2 to T-1 Primary)	1 day	Fri 9/19/14	Fri 9/19/14																														
213		Beam Dump Power	31 days	Mon 8/18/14	Mon 9/29/14																					Beam Dump Power									
214		Offline (T-6 to T-8 Primary)	3 days	Mon 8/18/14	Wed 8/20/14																														
217		Offline (T-5 to T-6 Primary)	4 days	Wed 9/17/14	Mon 9/22/14																														
220		Offline (T-6 Secondary)	5 days	Tue 9/23/14	Mon 9/29/14																														
223		Hall B	31 days	Mon 8/18/14	Mon 9/29/14																					Hall B									
224		Utility Power	31 days	Mon 8/18/14	Mon 9/29/14																					Utility Power									
225		Offline (T-6 to T-8 Primary)	3 days	Mon 8/18/14	Wed 8/20/14																														
228		Offline (T-5 to T-6 Primary)	4 days	Wed 9/17/14	Mon 9/22/14																														
231		Offline (T-6 Secondary)	5 days	Tue 9/23/14	Mon 9/29/14																														
234		Clean Power	15 days	Mon 9/1/14	Fri 9/19/14																					Clean Power									
235		Offline (T-2 Switchboard)	1 day	Mon 9/1/14	Mon 9/1/14																														
238		Offline (T-2 Secondary)	3 days	Tue 9/2/14	Fri 9/5/14																														
241		Offline (T-3 to T-2 Primary)	2 days	Wed 9/3/14	Fri 9/5/14																														
244		Offline (T-2 to T-1 Primary)	1 day	Fri 9/19/14	Fri 9/19/14																														
247		System Power	12 days	Mon 9/8/14	Tue 9/23/14																					System Power									
248		Offline (T-5 Switchboard)	1 day	Mon 9/8/14	Mon 9/8/14																														
251		Offline (T-5 Secondary)	11 days	Tue 9/9/14	Tue 9/23/14																														
254		Offline (T-12 to T-5 Primary)	5 days	Wed 9/10/14	Tue 9/16/14																														
257		Offline (T-5 to T-6 Primary)	4 days	Wed 9/17/14	Mon 9/22/14																														
260		Hall C	15 days	Mon 9/1/14	Fri 9/19/14																					Hall C									
261		Utility Power	6 days	Mon 9/1/14	Mon 9/8/14																					Utility Power									
262		Offline (T-3 Secondary)	6 days	Mon 9/1/14	Mon 9/8/14																														
265		Offline (T-4 to T-3 Primary)	2.5 days	Mon 9/1/14	Wed 9/3/14																														
268		Offline (T-3 to T-2 Primary)	2.5 days	Wed 9/3/14	Fri 9/5/14																														

Project: ESRAdvance
Date: Thu 7/17/14

Facility Outage

Region Outage

Outage

Generator Use

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Progress

ID	Task Mode	Task Name	Duration	Start	Finish	Jul 6, '14			Jul 20, '14			Aug 3, '14			Aug 17, '14			Aug 31, '14			Sep 14, '14			Sep 28, '14			Oct 12, '14		
						S	T	M	F	T	S	W	S	T	M	F	T	S	W	S	T	M	F	T	S	W	S	T	M
271		Clean Power	15 days	Mon 9/1/14	Fri 9/19/14																								
272		Offline (T-3 to T-2 Primary)	2.5 days	Wed 9/3/14	Fri 9/5/14																								
275		Offline (T-2 Switchboard)	1 day	Mon 9/1/14	Mon 9/1/14																								
278		Offline (T-2 Secondary)	3 days	Tue 9/2/14	Fri 9/5/14																								
281		Offline (T-2 to T-1 Primary)	1 day	Fri 9/19/14	Fri 9/19/14																								
284		System Power	9 days	Mon 9/8/14	Thu 9/18/14																								
285		Offline (T-1 Switchboard)	1 day	Mon 9/8/14	Mon 9/8/14																								
288		Offline (T-1 Secondary)	8 days	Tue 9/9/14	Thu 9/18/14																								
291		Offline (T-1 to T-12 Primary)	1 day	Tue 9/9/14	Tue 9/9/14																								
294		QWEAK Power	6 days	Tue 9/9/14	Tue 9/16/14																								
295		Offline (T-1 to T-12 Primary)	1 day	Tue 9/9/14	Tue 9/9/14																								
298		Offline (T-12 to T-5 Primary)	5 days	Wed 9/10/14	Tue 9/16/14																								

Project: ESRAdvance
Date: Thu 7/17/14

Facility Outage

Split

External Milestone

Duration-only

Deadline

Region Outage

Milestone

Inactive Task

Manual Summary Rollup

Progress

Outage

Summary

Inactive Milestone

Manual Summary

Start-only

Generator Use

Project Summary

Inactive Summary

Start-only

Task

External Tasks

Manual Task

Finish-only
