

Untitled Gantt Project

Apr 17, 2020

<http://>

Project manager

Project dates

Jun 16, 2020 - Aug 25, 2020

Completion

0%

Tasks

59

Resources

0

Tasks

| Name | Begin date | End date |
|---|------------|----------|
| 2 Week Return Notic | 6/16/20 | 6/29/20 |
| 2 Week Restore Period | 6/30/20 | 7/13/20 |
| Lock Ups | 6/30/20 | 7/13/20 |
| CEBAF Open | 6/30/20 | 6/30/20 |
| INJ Locked Up | 7/1/20 | 7/13/20 |
| NL Locked Up | 7/2/20 | 7/13/20 |
| SL/BSY Lock Up | 7/3/20 | 7/13/20 |
| Hall A Lock Up | 7/8/20 | 7/8/20 |
| Hall B Lock Up | 7/8/20 | 7/8/20 |
| Hall C Lock Up | 7/8/20 | 7/8/20 |
| Hall D Lock Up | 7/8/20 | 7/8/20 |
| Cryo | 6/28/20 | 7/3/20 |
| 4.5k Reroute for Repair | 6/28/20 | 6/29/20 |
| Pull 4.5k Return Bypass U Tube | 6/30/20 | 6/30/20 |
| INJ/NL Pumpdown Start | 7/1/20 | 7/1/20 |
| <i>Start filling INJ/C100 Modules First</i> | | |
| <i>Reinstall 4.5k U Tube</i> | | |
| SL/LERF Pumpdown | 7/2/20 | 7/2/20 |
| <i>Finish filling INJ/NL</i> | | |
| <i>Start filling C100's</i> | | |
| Pumpdown/Filling Complete | 7/3/20 | 7/3/20 |
| <i>Pumpdown and Filling Complete</i> | | |
| SSG | 6/30/20 | 7/8/20 |
| SA Camera Fix | 6/30/20 | 6/30/20 |
| Sweep Changes | 7/1/20 | 7/1/20 |
| MBSY1C Troubleshooting | 7/8/20 | 7/8/20 |


Tasks

| Name | Begin date | End date |
|--|------------|----------|
| EES IC | 6/30/20 | 7/1/20 |
| Standard HCO | 6/30/20 | 7/1/20 |
| EES RF | 6/30/20 | 7/5/20 |
| Repairs and HCO | 6/30/20 | 7/1/20 |
| INJ/NL Recovery | 7/2/20 | 7/3/20 |
| Separator Recovery | 7/3/20 | 7/3/20 |
| SL Recovery | 7/3/20 | 7/4/20 |
| Energy Push | 7/4/20 | 7/5/20 |
| Installation | 6/30/20 | 7/1/20 |
| Tunnel Walkthrough | 6/30/20 | 6/30/20 |
| <i>Checking and fixing water leaks</i> | | |
| HCO | 7/1/20 | 7/1/20 |
| EES DC | 6/30/20 | 7/8/20 |
| Inspections and INJ Trims | 6/30/20 | 6/30/20 |
| Main Machine Trims | 7/1/20 | 7/3/20 |
| ARC Box Supply Restore | 7/3/20 | 7/4/20 |
| Hall Power Supplies | 7/8/20 | 7/8/20 |
| SRF | 7/2/20 | 7/2/20 |
| 1L25 FE Measurements | 7/2/20 | 7/2/20 |
| Facilities | 6/30/20 | 7/1/20 |
| Belt/Filter Repairs | 6/30/20 | 7/1/20 |
| Gun | 6/30/20 | 7/1/20 |
| Reactivate Cathode | 6/30/20 | 7/1/20 |

Tasks

| Name | Begin date | End date |
|---|------------|----------|
| Cathode Rotatation (PQB) <i>After heat and reactivation of cathode. PQB folks and CIS will need some time to realign the cathode rotation.</i> | 7/1/20 | 7/1/20 |
| Beam Operations | 7/1/20 | 7/13/20 |
| Warm RF INJ | 7/1/20 | 7/1/20 |
| INJ Restore | 7/2/20 | 7/3/20 |
| PQB Verification | 7/3/20 | 7/3/20 |
| 1R | 7/4/20 | 7/4/20 |
| 2R | 7/5/20 | 7/5/20 |
| INJ Checks / Optics Checks | 7/6/20 | 7/6/20 |
| 6R | 7/7/20 | 7/7/20 |
| 5C | 7/8/20 | 7/8/20 |
| Beam Studies | 7/9/20 | 7/11/20 |
| BCM Cal HC 1st Pass | 7/9/20 | 7/9/20 |
| Arc1 M5,6 Download | 7/9/20 | 7/9/20 |
| Rematch | 7/10/20 | 7/11/20 |
| Hall Dumplette Tuning | 7/12/20 | 7/13/20 |
| 6 Weeks Physics | 7/14/20 | 8/24/20 |

Gantt Chart

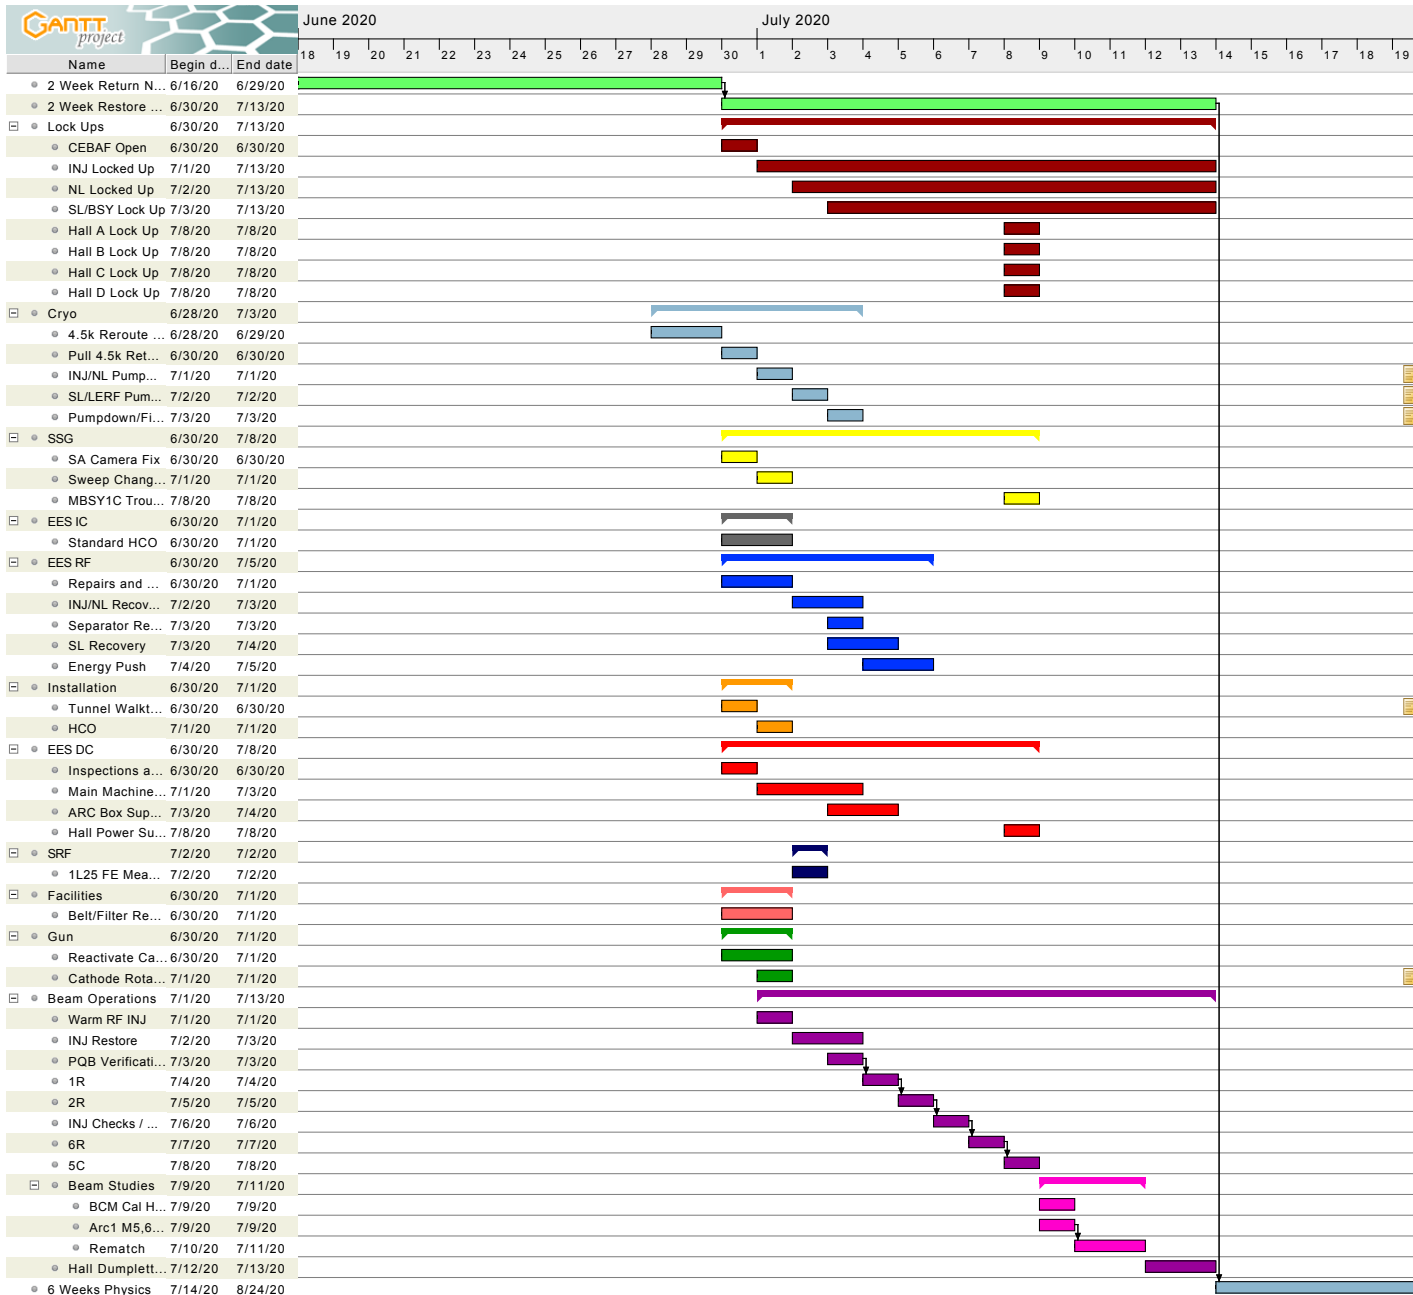

Resources Chart

